REDEEMER CHURCH

Renovation Schedule
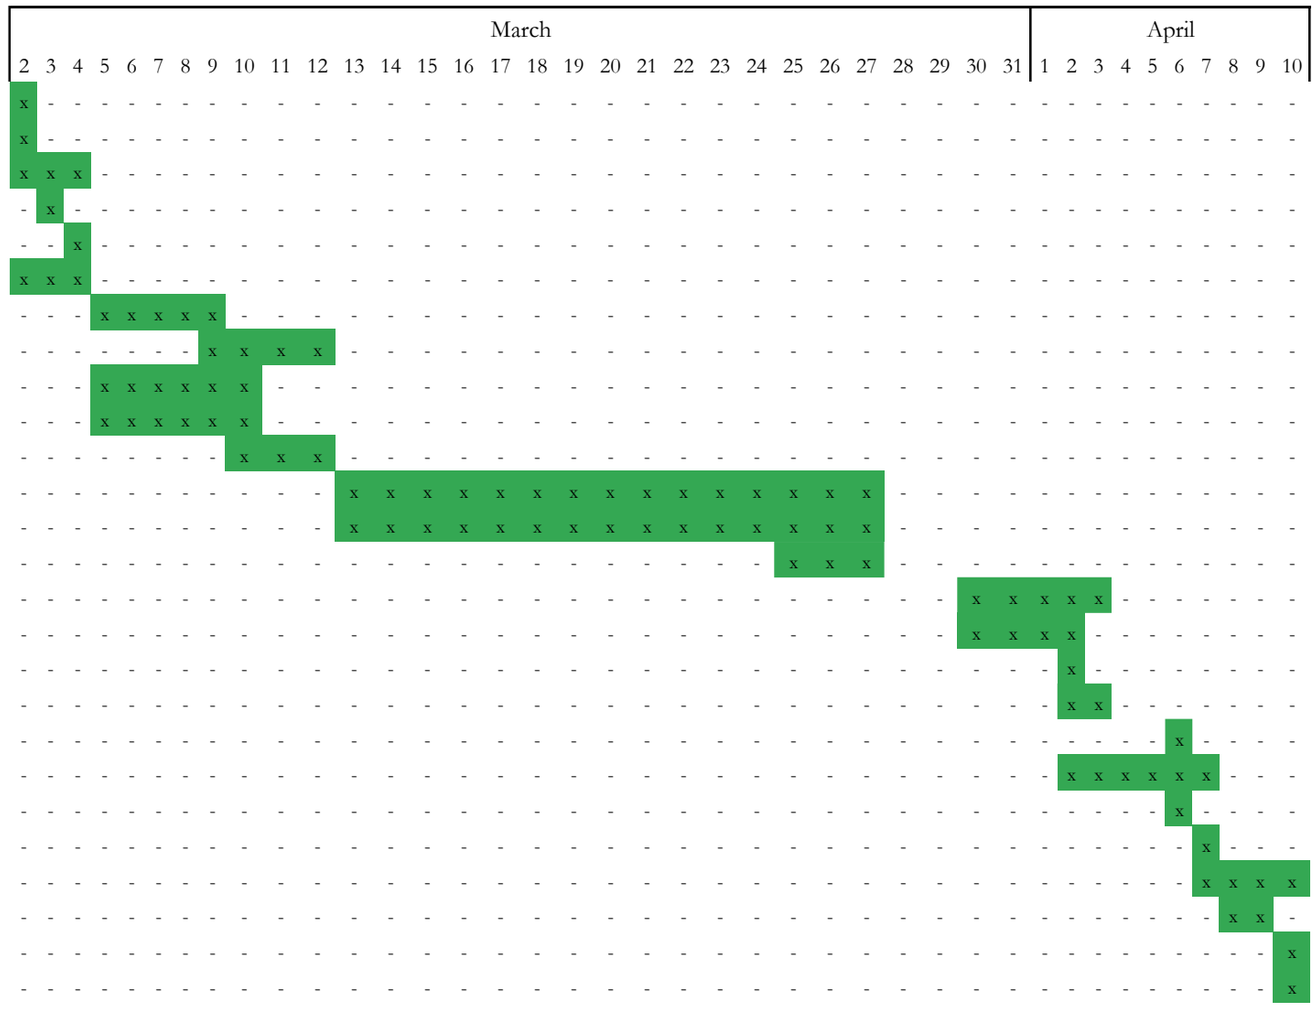
Activity	Start	Finish
Install Temporary Protections	03-02	03-02
Move Piano	03-02	03-02
Remove Pews, clear closet and misc. items	03-02	03-04
Organ removal	03-03	03-03
Chancel demo	03-04	03-04
Carpet demo	03-02	03-04
Expansion joints/ drywall work	03-05	03-09
Paint Narthex, Library, Coat room	03-09	03-12
Chancel framing/decking	03-05	03-10
Sound Rough ins	03-05	03-10
Drywall finishing	03-10	03-12
Pew Painting	03-13	03-27
Sanctuaury Painting	03-13	03-27
Valence lighting	03-25	03-27
Pew wood polishing	03-30	04-03
Carpet install	03-30	04-02
Electrical Finishes	04-02	04-02
Sound Finishes	04-02	04-03
Piano Placement	04-06	04-06
Sound Booth	04-02	04-07
Pew/Piano Placement	04-06	04-06
Temp Protection removal	04-07	04-07
Punchlist	04-07	04-10
Final Clean	04-08	04-09
Piano tuning	04-10	04-10
Ready for worship!	04-10	04-10
